

GREENPORT SCHOOL PROJECT- B & C

ROTC: Abatement complete

New switch gear: Installed in final location currently wiring in switch gear.

Office 110: Abatement complete.

Chorus room: Demo complete, mechanical installing duct work currently.

Multipurpose room: Upcoming.

Auto-Shop: Mechanical demoing existing duct work, abatement complete, Demo complete.

Woodshop: Mechanical demoing existing duct work.

2nd Floor bathrooms: Demoed ceilings, fixtures, and removing wall tile currently.

2nd Floor lockers: Lockers removed.

2nd Floor corridor/ classroom floors: Floor is being abated currently.

227 Resource room: Started removing ceiling.

3rd Floor bathrooms: Demoed ceilings, fixtures, and removing wall tile currently.

3rd Floor lockers: Lockers removed.

3rd Floor corridor/ classroom floors: Floor abatement complete new floors are being installed.

315 Science room: Demo complete, floor abatement complete.



305 Classroom: Demo complete.

Gym Addition: electrical hanging conduit, priming and painting currently going on.

UV- mechanical work: All UV's are demoed and out of the building, all relief air louvers are installed, all duct work in classroom ceilings are installed.



GREENPORT SCHOOL PROJECT- B & C

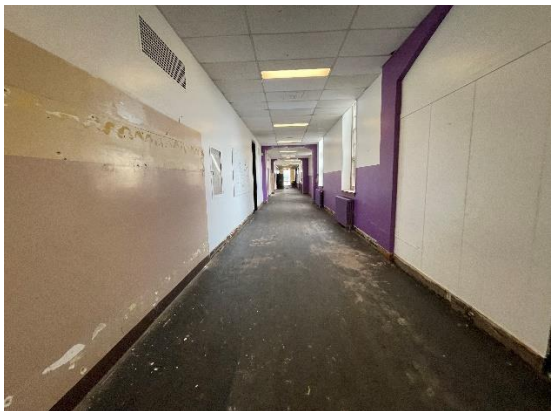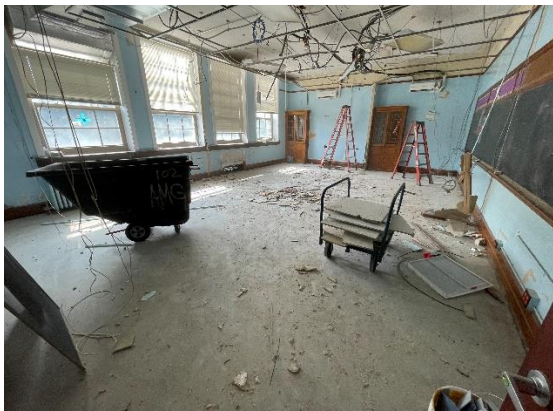

GREENPORT UNION FREE SCHOOL DISTRICT

DATES: 6/2/2023-7/19/2023

GREENPORT SCHOOL PROJECT- B & C

