

GREENPORT SCHOOL PROJECT-A & C

PROJECT-A

Locker rooms:

All lockers have been installed in both the girls and boy's locker rooms.

Lockers have been tagged by the installer.

SCC working with Clearview and district to schedule a time to perform the new floor in the girl's locker room, wall and door in the boy's locker room, and base cove in both locker rooms.(After we receive an updated insurance policy.)

Masonry restoration:

Wednesday Belfor mobilized dropping off a lift and porta potty in the areas discussed with the district.

PROJECT-C

95% of all drop ceiling speaker tiles are in place.

All J hooks on the 1-3rd floor have been installed in the hallway ceilings.


All room penetrations for running cables going into rooms off the corridors are complete.

All junction boxes for cameras on the interior of the building have been put in place.

The start of running fiber cables from the 3rd floor to the basement.



Before

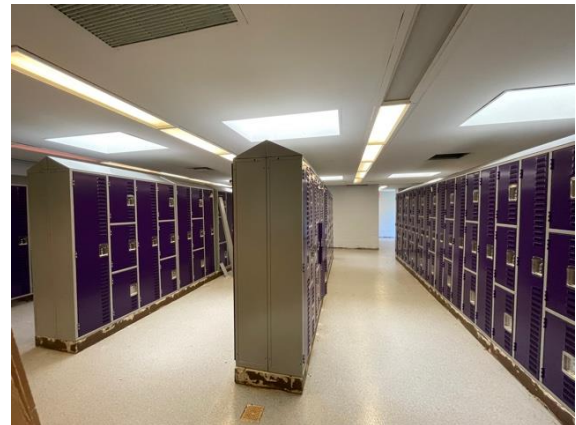

After

GREENPORT SCHOOL PROJECT-A & C



Before



After



Drop ceiling speakers



Camera junction boxes
